

Dokumen Handover Proyek Pixel Komunika

Atribut	Nilai
Versi dokumen	1.0
Tanggal handover	Selasa, 1 September 2026
Penulis	Kris Adiwinata — Webekspres
Repo	Webekspres/pixel-komunika
Branch aktif pengembangan	dev
Alur promosi	dev → staging → main

Daftar Isi

- [Identitas Proyek](#)
- [Ringkasan Eksekutif](#)
- [Scope Produk & Referensi Dokumen](#)
- [Progress per Sprint & Fase](#)
- [Matriks MVP: Selesai vs Belum](#)
- [Fitur Belum Diimplementasi / Ditunda](#)
- [Arsitektur Teknis](#)
- [Panduan Setup & Operasional](#)
- [Testing](#)
- [Halaman & Modul \(Quick Reference\)](#)
- [Data Contoh vs Production](#)
- [Risiko & Rekomendasi untuk Pengganti](#)
- [Glosarium & Kontak](#)
- [Checklist Serah Terima](#)

1. Identitas Proyek

Peran	Nama / Entitas
Klien	Pixel Komunika
Perwakilan klien (Product Owner)	Sylvi
Vendor pengembang	PT Webekspres Teknologi Indonesia
System Analyst	Sultan
Project Manager	Pak Endang
PIC POS (vendor eksternal)	Kak Rio
Developer handover	Kris Adiwinata

Deskripsi singkat: Website e-commerce B2B untuk pelanggan/reseller terverifikasi. Sistem mengelola katalog, harga partai/grosir, stok, order, invoice, pembayaran transfer manual, pengiriman, PPh 22, dan laporan. Website menjadi *source of truth* transaksi dan invoice; data produk/stok production bersumber dari POS; estimasi ongkir memakai Biteship Maps + Rates.

Stack teknologi:

- PHP 8.3+ / Laravel 13

- Blade + Livewire 4 + Tailwind CSS 4 + Vite
- MySQL / MariaDB
- Pest (testing)
- Queue, cache, session berbasis database/file (tanpa Redis di baseline)
- Production baseline: **shared hosting** milik klien

2. Ringkasan Eksekutif

Apa yang sudah bisa dilakukan hari ini

Alur penjualan website sudah **dapat dijalankan end-to-end** dengan data contoh: pelanggan mendaftar → admin menyetujui akun → pelanggan aktif melihat harga → menambah ke keranjang → checkout dengan perhitungan PPh 22 dan ongkir → order + invoice (HTML dan PDF) terbit → pelanggan mengunggah bukti transfer → admin memverifikasi pembayaran → admin memproses fulfillment (processing → packed → shipped → completed) → konfirmasi penerimaan via tautan publik atau auto-complete 5 hari kerja. Panel admin mencakup review pelanggan, pesanan, pembayaran, katalog, laporan omzet, audit log, dan pengaturan toko.

Progress MVP

Indikator	Nilai
Estimasi kelengkapan MVP	~75%
Test otomatis	146/146 lulus (706 assertions, per 1 September 2026)
Sprint 1–2	Selesai
Sprint 3	~95% (integrasi live pending)
Fase 6 (release/UAT)	Persiapan

Artinya praktis: fondasi bisnis dan teknis sudah kuat untuk demo, staging, dan UAT internal. Go-live production **belum aman** tanpa integrasi eksternal final.

Tiga blocker utama go-live

1. **POS production** — adapter saat ini masih *sample/mock*; kontrak HTTP final belum ditandatangani dengan vendor POS (PIC: Kak Rio).
2. **WhatsApp produksi** — notifikasi order baru dan tautan konfirmasi penerimaan masih driver `log / fake`, bukan provider sungguhan.
3. **Biteship live** — kode siap, tetapi default driver `mock`; aktivasi live membutuhkan `BITESHIP_API_KEY` dan verifikasi `BITESHIP_ORIGIN_AREA_ID`.

Rekomendasi prioritas next steps

1. Koordinasi Kak Rio untuk kontrak POS + *contract test* (lihat [POS FOLLOW UP.md](#)).
2. Smoke test di staging (`dev.store.pixelkomunika.com`) dengan skenario UAT.
3. Dapatkan keputusan klien untuk provider WhatsApp, template, dan credential.
4. Verifikasi origin area Biteship dengan alamat toko aktual.
5. Finalisasi keputusan terbuka OPN-006 (tarif/pembulatan PPh 22) dan OPN-008/OPN-022 (format invoice/reseller).
6. Sign-off daftar P0 di [MVP.md](#) — saat ini masih **Pending review** dari Sylvi, Sultan, dan Pak Endang.

3. Scope Produk & Referensi Dokumen

Hierarki dokumen

Dokumen	Peran	Lokasi
---------	-------	--------

BRD	Tujuan bisnis, scope, business rules, risiko, keputusan terbuka	requirements/BRD.md
FRD	Fungsi per modul, aktor, acceptance criteria	requirements/FRD.md
SRS	Arsitektur, stack, integrasi, keamanan, deployment	requirements/SRS.md
MVP	Daftar P0/Must Have dan acceptance gate 45 hari	requirements/MVP.md
ERD, Data Dictionary, User Flows, Sitemap	Desain data dan alur	design/
Sprint demo & checklist	Histori delivery per iterasi	SPRINT 1 DEMO.md , SPRINT 2 DEMO.md , sprints/SPRINT 3.md
Progress harian	Log iterasi dan blocker	PROGRESS.md
Review klien	Dokumen client-facing	client/DOKUMEN REVIEW DAN PERSETUJUAN KLIEN.md

BRD, FRD, dan SRS berstatus **Approved Working Baseline** sejak 27 Juli 2026. MVP masih **Candidate P0** — menunggu persetujuan final klien.

Tidak termasuk MVP (Out of Scope)

Kategori	Item
Infrastruktur	Microservices, Kubernetes, Redis wajib, VPS (kecuali shared hosting tidak cukup)
Produk	Aplikasi mobile native, marketplace multivendor, payment gateway
Integrasi	Perubahan internal POS, endpoint baru di sisi POS, Biteship order/pickup/label/tracking/webhook
Fitur P1	Reset password, pencarian/filter katalog lanjutan, export laporan CSV/XLSX
Fitur P2	Optimasi scale-out lanjutan di luar baseline traffic
Belum disetujui	Promo/voucher, skema poin loyalitas (OPN-020), pencatatan order channel WhatsApp (OPN-002)

4. Progress per Sprint & Fase



Fase / Sprint	Status	Bukti / Referensi
Fase 1 — Identity & access	Selesai	Registrasi, login, approval, guard akses
Fase 2 — Catalog, pricing, stok, data contoh	Selesai	Import sample, PPh 22 admin UI, partai/grosir
Fase 3 — Cart, checkout, shipping, order, invoice	Selesai	PDF invoice, gratis ongkir, konfirmasi penerimaan
Fase 4 — Payment, cancel/return, admin workflow	Selesai	Livewire admin payments, transisi status FRD
Fase 5 — Reporting, audit, sync resilience, security	Fondasi selesai	Audit UI, throttle; CI dependency scan belum

Fase 6 — Release readiness	Persiapan	CI deploy ada; UAT/sign-off belum
Sprint 1 — Auth, approval, katalog	Selesai	SPRINT 1 DEMO.md
Sprint 2 — Harga, PPh22, cart, checkout, invoice	Selesai	SPRINT 2 DEMO.md
Sprint 3 — POS outbox, payment, shipping, reports	~95%	sprints/SPRINT 3.md

5. Matriks MVP: Selesai vs Belum

Legenda status:

- **Selesai** — implementasi kode + test relevan lulus; siap UAT internal.
- **Parsial** — fondasi ada, tetapi go-live butuh keputusan/konfigurasi/integrasi eksternal.
- **Belum** — tidak ada implementasi atau sengaja ditunda (P1/P2).

MVP ID	Kapabilitas	Status	Catatan Implementasi
MVP-001	Registrasi dan autentikasi	Selesai	RegisteredUserController, AuthenticatedSessionController, rate limit login/register
MVP-002	Approval dan status pelanggan	Selesai	CustomerVerificationService, status pending/active/rejected/suspended
MVP-003	Hak akses guest, pending, reseller, admin	Selesai	Middleware EnsureActiveCustomer, EnsureAdmin; harga disembunyikan untuk guest/pending
MVP-004	Katalog dan pelengkap produk	Selesai	Import sample POS-like, enrichment admin, media library; sync POS real belum
MVP-005	Harga eceran, partai, dan grosir	Selesai	PriceCalculator, minimum partai global (default 5 unit/SKU), partai menang atas grosir
MVP-006	Integrasi master data dan inventory POS	Parsial	Scheduler + SamplePosSyncService; bukan HTTP POS production
MVP-007	Stok efektif dan rekonsiliasi	Parsial	inventory_ledger + outbox sale/return; ack masih sample simulator
MVP-008	Keranjang dan checkout	Selesai	CartService, Checkout Livewire, breakdown subtotal/PPh22/ongkir server-side
MVP-009	Order, invoice, riwayat, expiry	Parsial	Invoice HTML + PDF selesai; kirim via WhatsApp/email belum (OPN-022)
MVP-010	Pembayaran transfer manual	Selesai	Upload bukti, verifikasi admin, audit, signed URL preview
MVP-011	Pembatalan, retur, rekonsiliasi stok	Selesai	Cancel admin same-day + auto system; retur + restore stok + outbox return
MVP-012	Pengiriman kurir toko dan Biteship	Parsial	Kurir toko + gratis ongkir ≥ Rp1jt selesai; Biteship live butuh aktivasi driver
MVP-013	Laporan dasar	Selesai	/admin/reports, omzet dari status shipped/completed

MVP-014	Audit dan penanganan gangguan	Parsial	AuditLogger + UI search; modul audit FRD penuh masih Proposed
MVP-015	Security dan authorization	Selesai	CSRF, policies, rate limit, private upload, throttle checkout/upload
MVP-016	Release readiness	Parsial	CI deploy staging/main ada; UAT, training, sign-off, contract test belum
MVP-017	Ambang klasifikasi dan PPh 22	Parsial	Formula $(basis / 1,11) \times \text{tarif selesai}$; tarif multi-klasifikasi & pembulatan OPN-006
MVP-018	Notifikasi order baru admin	Parsial	Badge merah + notifikasi DB selesai; WhatsApp stub (log/fake)
MVP-019	Reseller dan channel pemesanan	Parsial	Reseller via website selesai; order WhatsApp OPN-002 belum diputuskan
MVP-020	Retensi bukti pembayaran	Selesai	retain_until 5 tahun, disk privat payment-proofs

Ringkasan numerik: 11 selesai · 9 parsial · 0 belum total (semua P0 punya fondasi kode).

6. Fitur Belum Diimplementasi / Ditunda

A. Integrasi eksternal (blocker go-live)

Integrasi	Status kode	Yang dibutuhkan
POS HTTP production	SamplePosSyncService + outbox	Kontrak endpoint, auth, payload, contract test — POS_FOLLOW_UP.md
WhatsApp produksi	LogWhatsAppNotifier / FakeWhatsAppNotifier	Provider, template, credential, retry — OPN-023
Biteship live	BiteshipShippingService siap	Set SHIPPING_DRIVER=biteship, API key, origin area ID — OPN-021
Email transactional	Mailer Laravel default (log)	Provider + template kirim invoice — OPN-022

B. Requirement FRD status Proposed / P1

Item	Prioritas	Keterangan
Reset password	P1	Route belum ada — SITEMAP.md §6
Search/filter katalog lanjutan	P1	Filter dasar ada di /produk; halaman terpisah ditunda
Export laporan CSV/XLSX	P1/TBD	Format belum disepakati
Audit modul lengkap (FR-AUD-001-004)	Proposed	AuditLogger partial; correlation ID & redaksi secret belum penuh
Idempotency checkout (FR-CART-007)	Proposed	orders.idempotency_key ada; UI/retry belum

C. Keputusan bisnis terbuka (OPN)

ID	Topik	Status	Dampak ke kode
----	-------	--------	----------------

OPN-002	Pencatatan order WhatsApp	Partially resolved	Channel WA order belum diimplementasi
OPN-005	Kontrak API POS final	Partially resolved	Adapter sample; ganti saat kontrak final
OPN-006	Tarif PPh 22 multi-klasifikasi & pembulatan	Formula resolved; rate/rounding open	config/store.php — strategy max, rounding half_up provisional
OPN-008	Format nomor invoice	Partially resolved	Penomoran otomatis ada; awalan/format final TBD
OPN-010	Tarif kurir toko per area	Threshold/H+1 resolved	StoreCourierRate — nilai per kecamatan perlu data klien
OPN-014	Order gabungan — ongkir & propagasi resi	Partially resolved	shipment_group_code otomatis; pembebanan ongkir TBD
OPN-015	Audit trail & scaling baseline	Open	BR-027-029 belum disetujui penuh
OPN-019	Koneksi POS production + contract test	Partially resolved	Go-live diblokir tanpa ini
OPN-020	Provider WA konfirmasi, kalender libur, poin	Partially resolved	Tautan konfirmasi ada; poin belum; holidays array kosong
OPN-021	Produk besar, fallback berat/dimensi Biteship	Partially resolved	Origin default ada di .env.example
OPN-022	Format NPWP/reseller, channel kirim invoice	Partially resolved	PDF + preview web selesai; kirim WA/email belum
OPN-023	Provider WhatsApp notifikasi admin	Partially resolved	Stub driver aktif


Detail lengkap: [BRD §15](#).

D. Fase 6 belum selesai

- Contract test POS dan Biteship
- Smoke test staging terstruktur
- Dependency vulnerability scan di CI (NFR-SEC-010)
- UAT dengan Sylvi + training admin
- Go-live sign-off formal
- Verifikasi shared hosting: cron, log, backup, rollback

7. Arsitektur Teknis

Diagram alur data

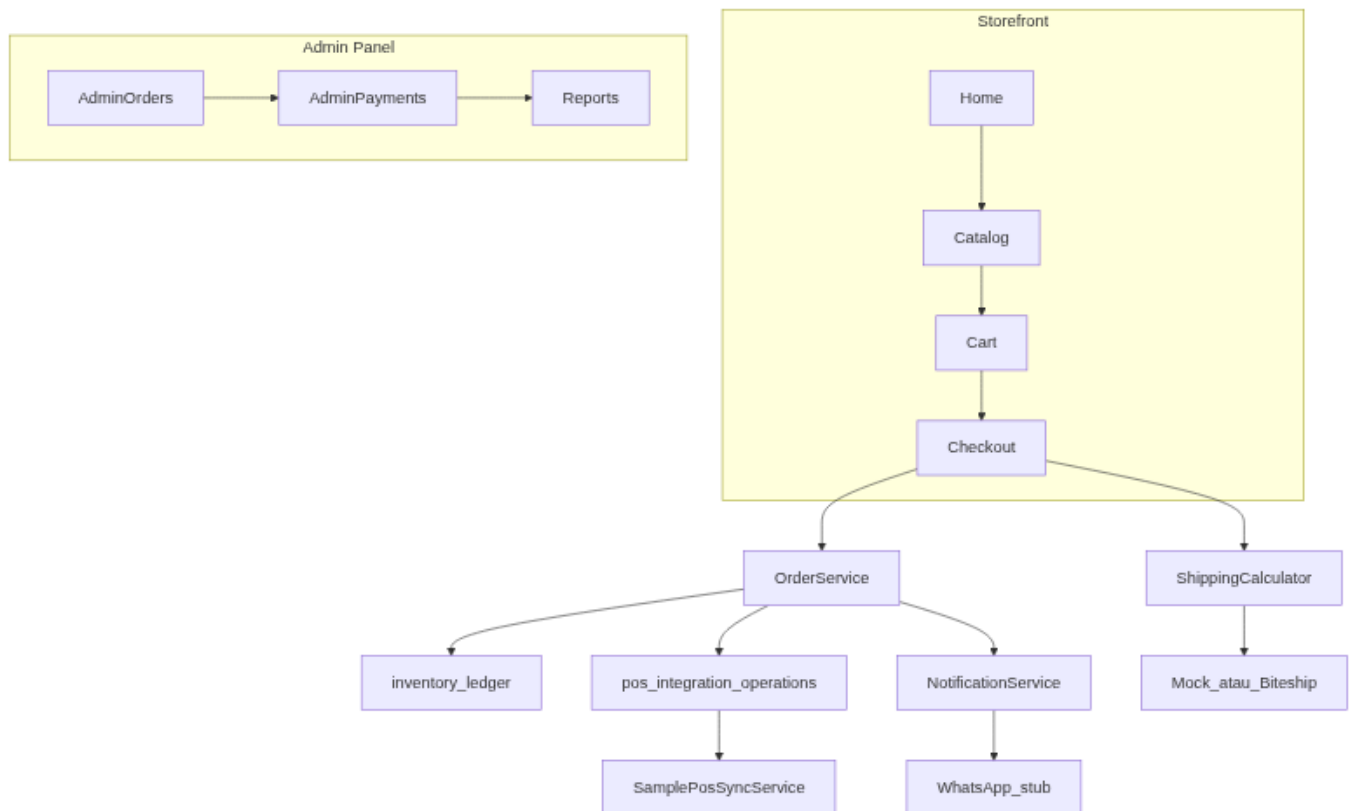

Layer kode

Layer	Lokasi	Isi
UI (Livewire)	app/Livewire/	17 komponen — storefront, customer, admin
Controllers	app/Http/Controllers/	Auth, account, invoice, receipt, admin, API area/POS
Domain services	app/Domains/	Pricing, Order, POS, Audit, Reporting, Notifications, Catalog, Customer
Application services	app/Services/	Cart, Order, Payment, Shipping
Models	app/Models/	33 model Eloquent
Routes	routes/web.php, routes/api.php	Web + POS read-only API
Commands	app/Console/Commands/	8 command terjadwal
Views	resources/views/	Blade + Livewire templates
Tests	tests/	42 file test Pest (Feature + Unit)

Domain services utama

Service	File	Fungsi
PriceCalculator	app/Domains/Pricing/PriceCalculator.php	Harga grosir/partai, PPh 22
OrderService	app/Services/OrderService.php	Place order, cancel, retur, stok

PaymentService	app/Services/PaymentService.php	Upload & verifikasi bukti
FulfillmentService	app/Domains/Order/FulfillmentService.php	Transisi status, shipment
PosOutboxService	app/Domains/PosIntegration/PosOutboxService.php	Antrean laporan ke POS
SamplePosSyncService	app/Domains/PosIntegration/SamplePosSyncService.php	Adapter sample (ganti untuk production)
ReportingService	app/Domains/Reporting/ReportingService.php	Omzet & PPh 22
AuditLogger	app/Domains/Audit/AuditLogger.php	Jejak audit aksi kritis
NotificationService	app/Domains/Notifications/NotificationService.php	Notifikasi DB + WhatsApp stub

Pola arsitektural penting

- **Modular monolith** — bukan microservices; domain logic di `app/Domains/` .
- **Stok efektif** — `inventory_snapshots` + `inventory_ledger` ; mutasi pakai `DB::transaction` + `lockForUpdate()` .
- **POS outbox** — laporan penjualan/retur ke `pos_integration_operations` ; dispatcher tiap 5 menit; idempotency via `external_reference` .
- **Enrichment lokal** — nama tampilan, media, berat, dimensi tidak ditimpa sync POS.
- **Shipping driver switch** — binding di `AppServiceProvider` : `mock` (default) atau `biteship` .
- **WhatsApp driver switch** — `log` (default) atau `fake` untuk testing.

Middleware & keamanan

Middleware	Fungsi
EnsureAdmin	Guard panel admin
EnsureActiveCustomer	Guard checkout & riwayat pesanan
VerifyPosApiToken	Auth API POS read-only
Throttle	Login/register 5/menit; checkout 10/menit; upload bukti 5/menit

Policies: `OrderPolicy` , `PaymentProofPolicy` , `CustomerProfilePolicy` .

8. Panduan Setup & Operasional

Prasyarat

- PHP 8.3+, Composer, Node.js, MySQL/MariaDB
- Database: `pixelkomunika_db` (default)

Setup development

```
git clone https://github.com/Webekspres/pixel-komunika.git
cd pixel-komunika
git checkout dev

composer install
cp .env.example .env
php artisan key:generate
# Sesuaikan DB_* di .env jika perlu
php artisan migrate
npm install
```

```
npm run build

# Jalankan server + queue + vite sekaligus
composer run dev

# Import data contoh (idempotent)
php artisan catalog:import-sample

# Verifikasi
composer test
curl http://localhost:8000/health
```

Environment variables kunci

Variable	Fungsi	Default dev
DB_*	Koneksi database	mysql / pixelkomunika_db
APP_TIMEZONE	Zona waktu order/expiry	Asia/Jakarta
POS_API_TOKEN	Auth API baca order POS	kosong
BITESHIP_API_KEY	API key Biteship	kosong
BITESHIP_ORIGIN_AREA_ID	Origin pengiriman	ada di .env.example
SHIPPING_DRIVER	mock atau biteship	mock
WA_DRIVER	log atau fake	log
STORE_*	Identitas toko	Pixel Komunika defaults
PPH22_DIVISOR	Pembagi dasar PPh 22	1.11
STORE_FREE_SHIPPING_THRESHOLD	Ambang gratis ongkir kurir toko	1000000
ORDER_AUTO_COMPLETE_WORKDAYS	Auto-complete setelah shipped	5
PAYMENT_PROOF_RETAIN_YEARS	Retensi bukti bayar	5

Kredensial production **tidak** disimpan di repository.

Scheduler / cron production

Wajib di shared hosting via cron:

```
* * * * * cd /path/to/app && php artisan schedule:run >> /dev/null 2>&1
```

Jadwal di [routes/console.php](#) :

Command	Frekuensi	Fungsi
orders:auto-cancel-unpaid	Harian 00:05	Batalkan order unpaid kemarin
orders:auto-complete-shipped	Harian 00:15	Auto-complete shipped (skip TERKENDALA)
pos:sync-masters	Harian 01:00	Sync master data POS
pos:sync-stock	Harian 01:30	Sync stok POS

pos:dispatch-sale-reports	Tiap 5 menit	Kirim laporan penjualan
pos:dispatch-return-reports	Tiap 5 menit	Kirim laporan retur
notifications:dispatch-pending	Tiap 5 menit	Kirim notifikasi WhatsApp pending

Queue worker (bounded, shared hosting):

```
php artisan queue:work --stop-when-empty --tries=3
```

Deploy

Push ke branch `staging` atau `main` memicu GitHub Actions:

1. `composer install`
2. `php artisan test` (146 test)
3. Deploy via cPanel API ke path repository

Branch	Environment	Path repository
staging	Staging	/home/pixelkom/repositories/dev.store.pixelkomunika.com
main	Production	/home/pixelkom/repositories/store.pixelkomunika.com

Workflow: [.github/workflows/deploy.yml](#) .

Kebijakan branch: jangan push ke `dev` / `staging` / `main` tanpa permintaan eksplisit. Alur promosi: `dev` → `staging` → `main` .

Command artisan berguna

Command	Fungsi
catalog:import-sample	Import/upsert data contoh POS-like
pos:sync-masters	Sync master (manual)
pos:sync-stock	Sync stok (manual)
orders:auto-cancel-unpaid	Cancel unpaid (manual)
orders:auto-complete-shipped	Auto-complete (manual)

9. Testing

Atribut	Nilai
Framework	Pest 4 + Laravel plugin
File test	42 file (36 Feature, 5 Unit, 1 Example)
Total test	146 passed , 706 assertions
Perintah	<code>composer test</code> atau <code>php artisan test</code>

Area coverage kuat

- Auth, registrasi, rate limit
- Akses pelanggan (guest/pending/active)
- Storefront, katalog, harga grosir/partai

- Cart, checkout end-to-end, charge components, inventory ledger
- Pembayaran upload/approve/reject, retur stok
- Invoice PDF download & authorization
- Konfirmasi penerimaan publik (token)
- Shipping mock & Biteship error mapping
- Admin: dashboard, pelanggan, pesanan, pembayaran, katalog, pajak, laporan, settings, notifikasi, audit
- POS API read-only
- Auto-cancel unpaid, rate limit checkout/upload
- Import katalog idempotent, health check

Gap coverage

- Integrasi POS HTTP production (real adapter)
- WhatsApp provider production
- Email transactional
- Contract test Biteship live end-to-end di staging
- Dependency vulnerability scan CI

10. Halaman & Modul (Quick Reference)

Storefront & auth

Halaman	Path	Akses
Beranda	/	Semua
Katalog	/produk	Semua (harga sesuai hak)
Detail produk	/produk/{product}	Semua
Keranjang	/cart	Login (checkout: reseller aktif)
Daftar	/daftar	Guest
Masuk	/masuk	Guest
Konfirmasi penerimaan	/konfirmasi-penerimaan/{order}?token=...	Publik (token)

Area pelanggan

Halaman	Path	Akses
Ringkasan akun	/akun	Login
Profil	/akun/profil	Login
Alamat	/akun/alamat	Login
Checkout	/checkout	Reseller aktif
Daftar pesanan	/akun/pesanan	Reseller aktif
Detail pesanan + bukti bayar	/akun/pesanan/{order}	Pemilik order
Invoice / PDF	/akun/pesanan/{order}/invoice	Pemilik order

Area admin (/admin/*)

Halaman	Path
---------	------

Dashboard	/admin
Pelanggan	/admin/customers
Pesanan	/admin/orders
Pembayaran	/admin/payments
Produk & enrichment	/admin/products
Media	/admin/media
Kategori / Merek	/admin/categories, /admin/brands
Aturan PPh 22	/admin/tax-rules
Laporan	/admin/reports
Audit log	/admin/audit-logs
Pengaturan	/admin/settings

API

Endpoint	Auth	Fungsi
GET /api/areas/search	Login	Cari area pengiriman
GET /api/areas/districts	Login	Daftar kecamatan
GET /api/pos/orders/{order_number}	POS_API_TOKEN	Baca order untuk POS
GET /health	Publik	Health check DB

Halaman ditunda (bukan P0)

- Lupa/reset password (P1)
- Wishlist, notifikasi pelanggan
- About, FAQ, Contact terpisah

Detail lengkap: [SITEMAP.md](#).

11. Data Contoh vs Production

Konteks	Sumber data	Cara
Local development	Data contoh	php artisan catalog:import-sample, seeder
Staging / demo / UAT	Data contoh	Sama — boleh diulang (idempotent)
Production	POS real wajib	Ganti SamplePosSyncService dengan adapter HTTP final

Aturan penting:

- Data contoh **tidak boleh** menjadi sumber produk/stok production.
- SKU dan external ID data contoh stabil; import berulang tidak duplikasi atau menimpa enrichment lokal.
- Go-live diblokir tanpa contract test POS (OPN-019).
- Trigger akses POS: alur website berbasis data contoh sudah berjalan — koordinasi via Kak Rio.

12. Risiko & Rekomendasi untuk Pengganti

Prioritas berurutan

1. **POS** — Dapatkan dokumen kontrak dari Kak Rio; implementasi adapter HTTP; jalankan contract test master, stok, sale report, return report, acknowledgement, idempotency.
2. **Biteship** — Verifikasi `BITESHIP_ORIGIN_AREA_ID` dengan alamat toko; uji rates live di staging; set `SHIPPING_DRIVER=biteship`.
3. **WhatsApp** — Pilih provider; implementasi driver production; template "Cek Order masuk" dan tautan konfirmasi penerimaan.
4. **UAT staging** — Jalankan skenario dari SPRINT_1/2/3 demo docs dengan Sylvi.
5. **Keputusan bisnis** — Tutup OPN-006, OPN-008, OPN-010, OPN-014, OPN-020, OPN-022.
6. **Sign-off MVP** — Dapatkan persetujuan tertulis daftar P0 di MVP.md.
7. **Release** — Smoke test production, backup/rollback, training admin, go-live sign-off.

Risiko teknis

Risiko	Mitigasi
POS timeout → laporan ganda	Outbox + idempotency + external_reference sudah ada; uji skenario timeout
Shared hosting queue terbatas	--stop-when-empty worker; scheduler-based dispatch
PPh 22 salah setelah keputusan klien	Config <code>store.pph22</code> + admin tax rules; update test setelah OPN-006 final
Biteship down saat checkout	Fallback: minta pelanggan hubungi admin (OPN-016 resolved)

File penting untuk dibaca pertama

1. [PROGRESS.md](#) — log iterasi terbaru
2. [sprints/SPRINT_3.md](#) — checklist verifikasi Sprint 3
3. [POS_FOLLOW_UP.md](#) — daftar konfirmasi ke vendor POS
4. [AGENTS.md](#) — aturan agent, branch policy, destructive actions
5. [README.md](#) — setup cepat

13. Glosarium & Kontak

Istilah domain

Istilah	Arti
Reseller	Akun terdaftar yang disetujui admin; dapat melihat harga dan checkout
Partai	Harga khusus jika ≥ 1 SKU mencapai minimum global (default 5 unit); berlaku cart-wide
Grosir	Harga dengan minimum kuantitas per produk; kalah prioritas dari partai
PPh 22	Pajak penghasilan; $(\text{subtotal_klasifikasi} / 1,11) \times \text{tarif}$
TERKENDALA	Penanda order shipped yang menahan auto-complete scheduler
Outbox POS	Antrean operasi <code>WEB_SALE_REPORT</code> / <code>WEB_RETURN_REPORT</code> ke POS
Enrichment	Data lokal website (nama tampilan, media, berat) yang tidak ditimpa sync POS

Kontak

Peran	PIC	Catatan
-------	-----	---------

Product Owner klien	Sylvi	Persetujuan scope, UAT, go-live
PIC POS	Kak Rio	Kontrak API, akses sandbox/production
System Analyst	Sultan	Requirement, traceability
Project Manager	Pak Endang	Timeline, release governance
Developer handover	Kris Adiwinata	ka.webekspres@gmail.com

14. Checklist Serah Terima

Centang saat handover selesai:

- ☐ Akses repo GitHub dan branch policy (`dev` → `staging` → `main`) dijelaskan
- ☐ Perbedaan `.env.example` vs `secret production` dipahami
- ☐ Demo flow end-to-end dapat dijalankan di local/staging
- ☐ Test suite lulus (`composer test` — 146/146)
- ☐ Blocker eksternal terdokumentasi dengan PIC masing-masing
- ☐ Link ke BRD, FRD, SRS, MVP, ERD, user flows valid
- ☐ Cron/scheduler production dikonfigurasi di hosting
- ☐ Kredensial staging/production diserahkan via channel aman (bukan repo)
- ☐ Sylvi / Pak Endang / Sultan menerima dokumen ini

Dokumen ini adalah snapshot status per 1 September 2026. Untuk log iterasi harian, lihat [PROGRESS.md](#). Untuk requirement detail, selalu rujuk BRD/FRD/SRS sebagai sumber kebenaran.
